


19.10.2016


- I cleaned the vacuum chamber



- I tested the all M6 holes from the vacuumchamber

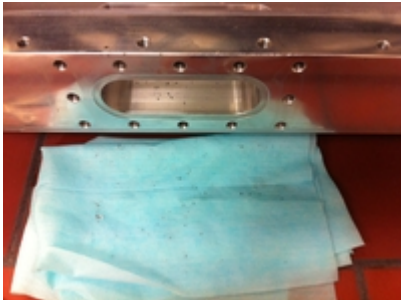

all threads are deep enough!

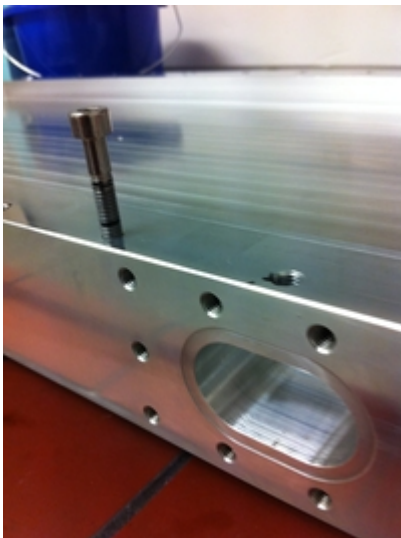


- 2x M4-breadboards (incouple and outcouple) and there spacers are done!
- I assembled the mounting with vitonballs and zerodur rods.



We need two vitonballs of each metal sheet side. Otherwise the mounting is to wobbly!



8x new sinkings for the vitonballs! If you fixed the mounting screws: tighten them crosswise!!!

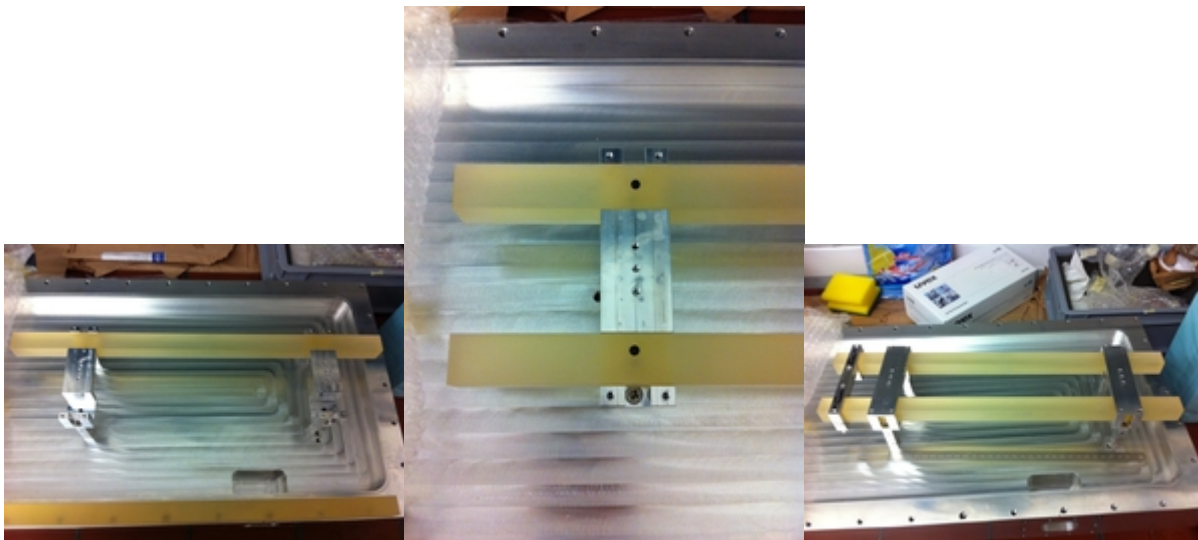

- Leaktest

positiv 😞

New weld!



From:
<https://iqwiki.iqo.uni-hannover.de/> - IQwiki

Permanent link:
https://iqwiki.iqo.uni-hannover.de/doku.php?id=groups:mg:project_ptb-cavity:labbook:2016-10:labbookentry-2016-10-19&rev=1477067898

Last update: **2016/10/21 16:38**

